

Power distribution

Keyman 	Crew
Jeff Korell	April Korell

Your team safely runs mains power to the A/V booth, the stage, and the active loudspeakers. Audio Cabling handles audio cables.

Before starting, review the team’s [DC-83](#) and Sheet 4-1 in the [schematics](#).

DC-83 — Saturday morning safety review

Reviewed by Ralph Ord on 5 October 2026. [Open the final PDF.](#)

Job Hazard Analysis

(Job Hazard Analysis Instructions (DC-83i) must be used while completing this form.)

PROJECT TITLE

CABR-2026-10 Assembly A/V

JOB DESCRIPTION

Power CW - setup and dismantling

JOB LOCATION

Imperial World Samrong - booth, stage and audience power

SCHEDULED START DATE

2026/10/10

EMERGENCY NUMBER(S)

093-019-4124 (Program Overseer Bo Nielsen)

ELIMINATION

SUBSTITUTION

ENGINEERING

ADMINISTRATIVE


PPE

JOB STEPS		HAZARDS	CONTROL METHODS		
Move PCS-2 power case		Ergonomic/safety: 50 kg rolling case; strain or crush injury.	Engineering/Admin: Use wheels, a clear route and helpers; gloves/work shoes. Assigned to: Jeff Korell		
Route booth, stage and audience power		Electrical/safety: Damaged cords, wet areas or trip hazards.	Elimination/Engineering: Reject damaged cords; keep clear of wet/baptism areas; cover crossings. Assigned to: Jeff Korell		
Connect to approved supply		Electrical: Shock, incorrect supply or overload.	Admin: Qualified person if panel work is needed; verify rating; no altered ground/overload. Assigned to: Jeff Korell		
Inspect and hand over circuits		Electrical/safety: Unexpected energization or loose covers.	Admin: Check routes/circuits; keep exits clear; tell teams before energizing. Assigned to: Jeff Korell		
Deenergize and remove after program		Electrical/safety: Shock or trips during rushed teardown.	Admin: Wait for crowd; power off before removal; qualified person for panel; inventory. Assigned to: Jeff Korell		
PREPARED BY	DATE PREPARED	REVIEWED BY	DATE REVIEWED	REVISED BY	DATE REVISED
JP Bourgeois	2026/09/24	Ralph Ord	2026/10/05		

Use additional forms as needed.

DC-83-E 4/22

Main reference — Sheet 4-1. Use it for venue outlets, stage power, stage monitors and the route to the A/V booth.

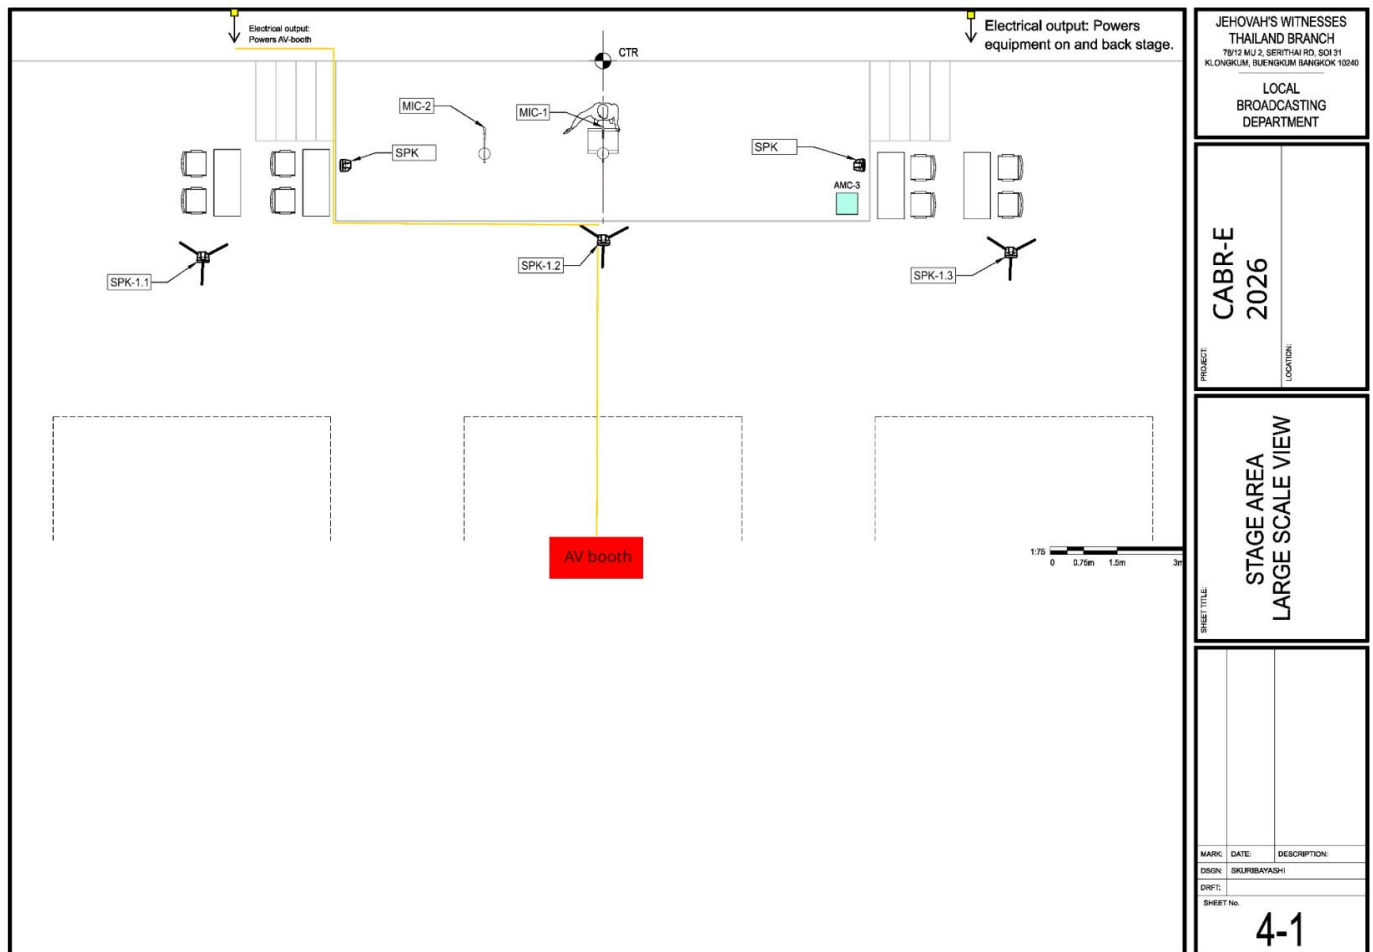

Safety:

Roll the 50 kg PCS-2 case on a clear route with helpers; wear work shoes and gloves.

Electrical work: Only a qualified person performs panel work or other work requiring a qualification. Never alter an equipment ground. Set aside damaged cords, avoid overloaded circuits, and keep power away from the baptism area and wet floors.

What your team does

1. Confirm the two approved venue outlets on Sheet 4-1 and verify supply ratings against the expected loads. Agree routes with Stage and Audio Cabling before laying mains cables through their work area.
2. From the left outlet, run the booth supply along the stage front and down the centre route to the A/V booth.
3. From the right outlet, run power for stage equipment, including both stage monitors. Coordinate final connections with Stage and Loudspeakers.
4. Confirm safe wall sockets for the lobby and Accounting speakers; run their mains supply and coordinate final connections with Loudspeakers.

5. Protect every floor crossing and inspect circuits, routes and cover edges; keep exits and participant paths clear. **Tell the teams before energizing any supply.** Jeff connects booth power only after A/V Booth's connection checks.
6. When power work is safely complete, check with Lacey and help Audio Cabling with the remaining cable work and floor crossings.

Where practical, keep mains power separate from audio cables; cross at **right angles** where they meet.

The venue wireless receivers at the stage may also need power; confirm this with the venue technician.

Follow the [confirmed dismantling teams and instructions](#). After the audience has cleared and the safety meeting has finished, let the teams shut down their equipment. **Jeff isolates and disconnects power before cords are removed.** Use a qualified person for panel work and inventory the power equipment.

Revision #10

Created 2026-09-26 09:00:34 UTC by JP

Updated 2026-10-05 08:42:48 UTC by Documentation-Open
